



# Downtown Streetlight and Pavement Rehabilitation Project

**City of Visalia**

# Public Kick-Off Meeting:

Wednesday, June 22, 2022  
6PM to 8PM

Visalia Convention Center,  
Sequoia Room



Downtown Visalia

# Public Kick-Off Meeting:

- Project Background & Update
- Phasing Plan
- Schedule

# Introductions:


- City of Visalia
- NV5 / Lockwood Agency / Yarbs Grading & paving
- A-C Electric




# Project Background



# Non-Decorative

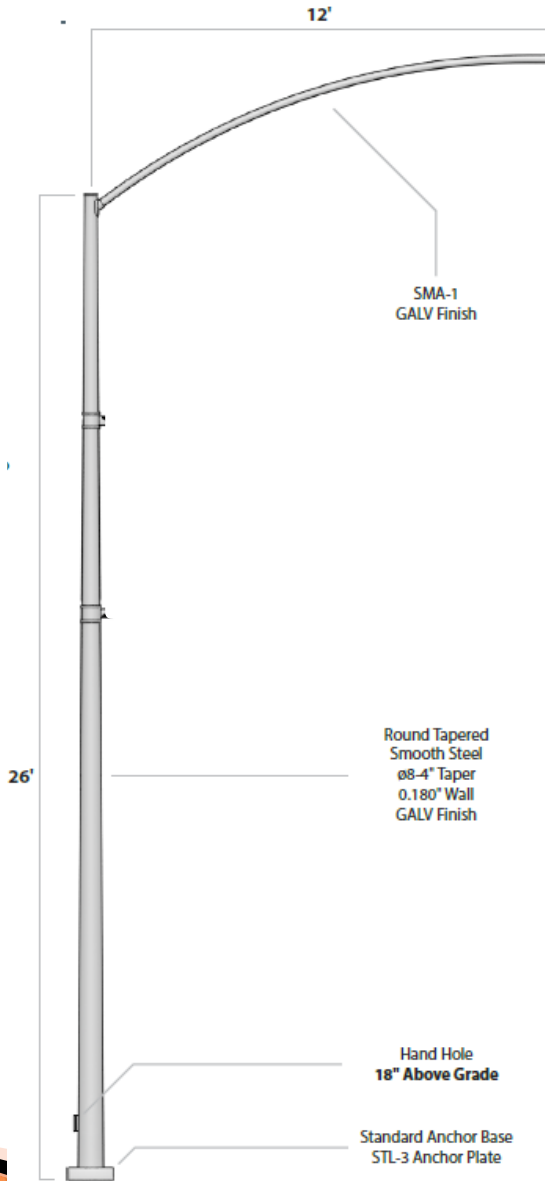

# Decorative

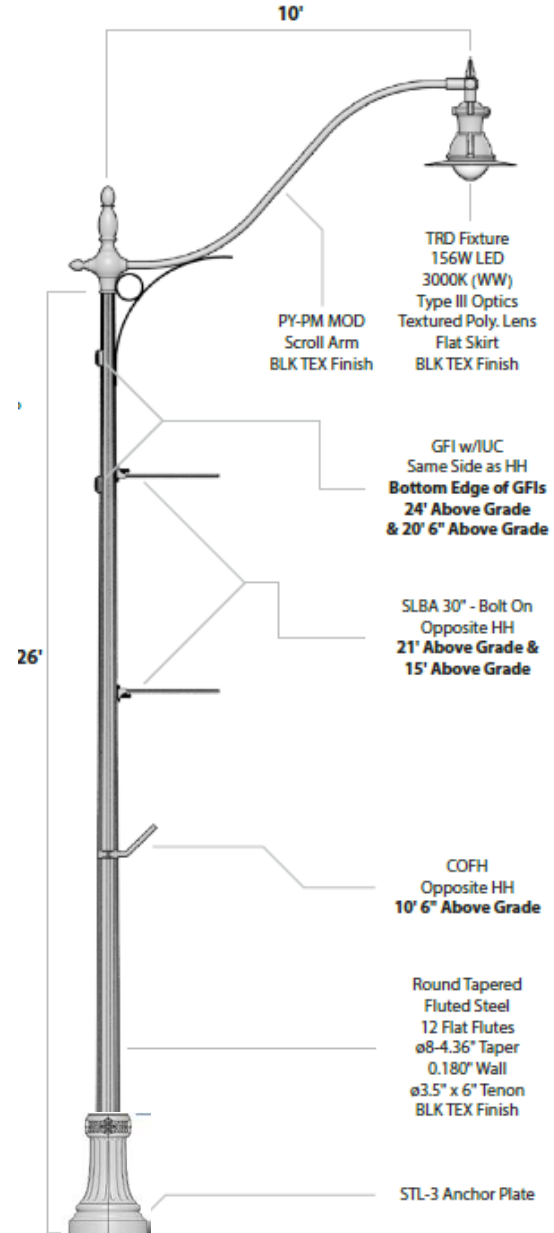

# Street Lighting


- Project Status

- Project Schedule

- Work Schedule
  - Sunday thru Thursdays
- Hours
  - 10PM to 6AM
- Construction Schedule
  - July 2022 through April 2023



# Street Lighting

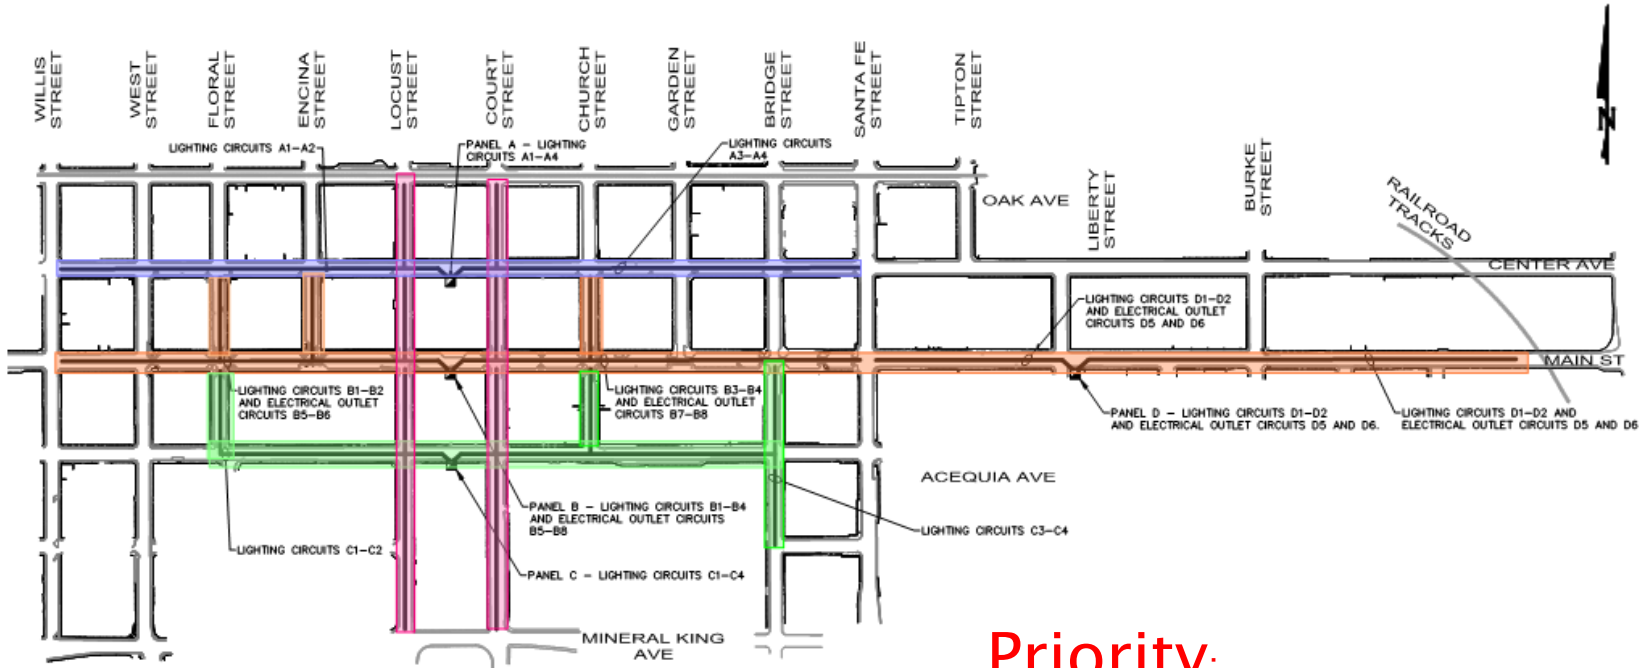

## Priority:

1. Main Street
2. Acequia Ave.
3. Center Ave.
4. Locust / Court Street (Caltrans)





# Sequence of Work Example



Streetlight trunk line



Street lighting service lateral




Concrete work / Curb ramps, Sidewalk, ADA parking stalls






Traffic detour routes

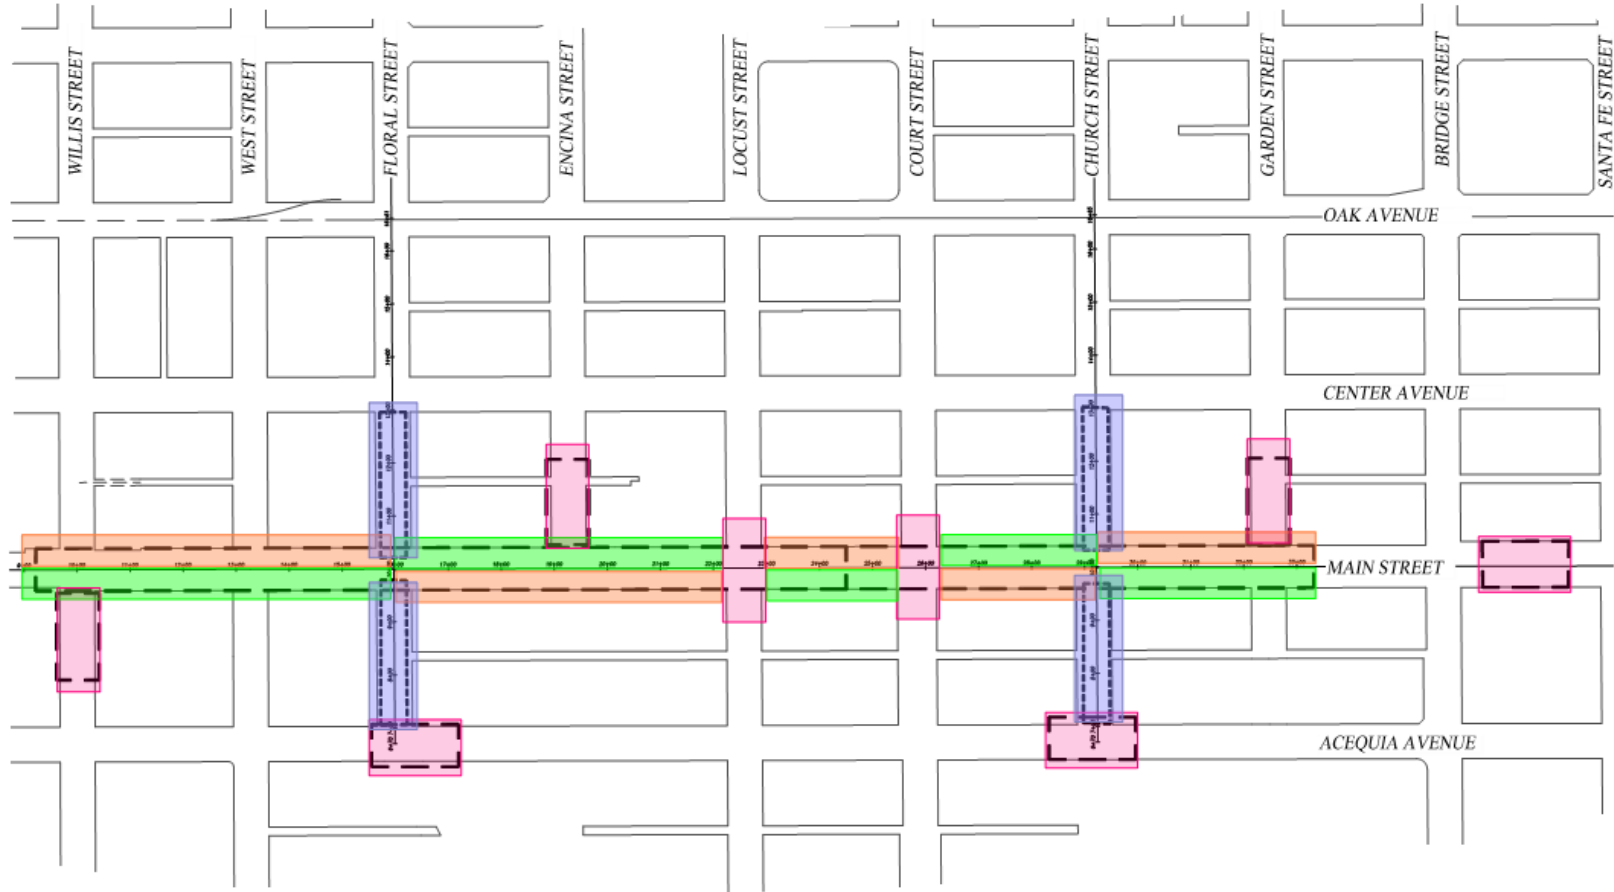

# Pavement Project



## LEGEND: (THIS SHEET ONLY)

-  Alternating Paving Application (2 Blocks per Night)
-  Alternative Bid Item
-  ADA Parking and Pedestrian Ramps Improvements



# Look Ahead Schedule – July 2022

- Potholing of existing utilities.
- Installation of Temporary lighting.
- Work will begin Main Street from Willis Street to Floral Street in an east to west direction (approx. 2-blocks per month for electrical work).
- Main Street – Willis to Santa Fe  
(Completion by November 2022)

# Public Outreach

- Weekly scheduled update meetings.
- Project Information posted on the City's social media.
- Press Releases.
- Text Notifications. Text **DTLighting** to **74121**
- Paper Notifications 48 hours prior to start of work.
- Portable Message Signs in place prior to closures.
- Construction Manager (NV5) will maintain a 24-hour hotline.

# Contact information

Frank Senteno  
**City Engineer, City of Visalia**  
(559) 713-4331  
[Frank.Senteno@Visalia.City](mailto:Frank.Senteno@Visalia.City)

Kirt Carr  
**NV5 Construction Manager**  
(559) 481-9255 (*24-Hour Contact*)  
[Kirt.Carr@NV5.com](mailto:Kirt.Carr@NV5.com)

# Q & A



# Rendering Image



# Rendering Image





# Rendering Image

